


South Memorial Parkway (US-231/SR-53) Improvements Project

District 3 Town Hall meeting
Dr. Jennie Robinson
August 29, 2016



“Restore our Roads”



Overview



Phase I

Memorial Parkway service roads, new parkway overpass bridge with intersection and new railroad bridge on Martin Road with completion by December 1, 2017 (September 1, 2017 for maximum incentive)

Phase II


Mainline and overpasses at Byrd Springs Road and Logan Drive/Lily Flagg Road with completion by June 1, 2019 (March 1, 2019 for maximum incentive)

What's the status?

- As of mid-August, project was about 35 percent complete at about 20 percent of time
- Phase II work will begin before Phase I complete
- Based on progress thus far, currently anticipating completion by maximum incentive deadlines

Project progress

Time Completion

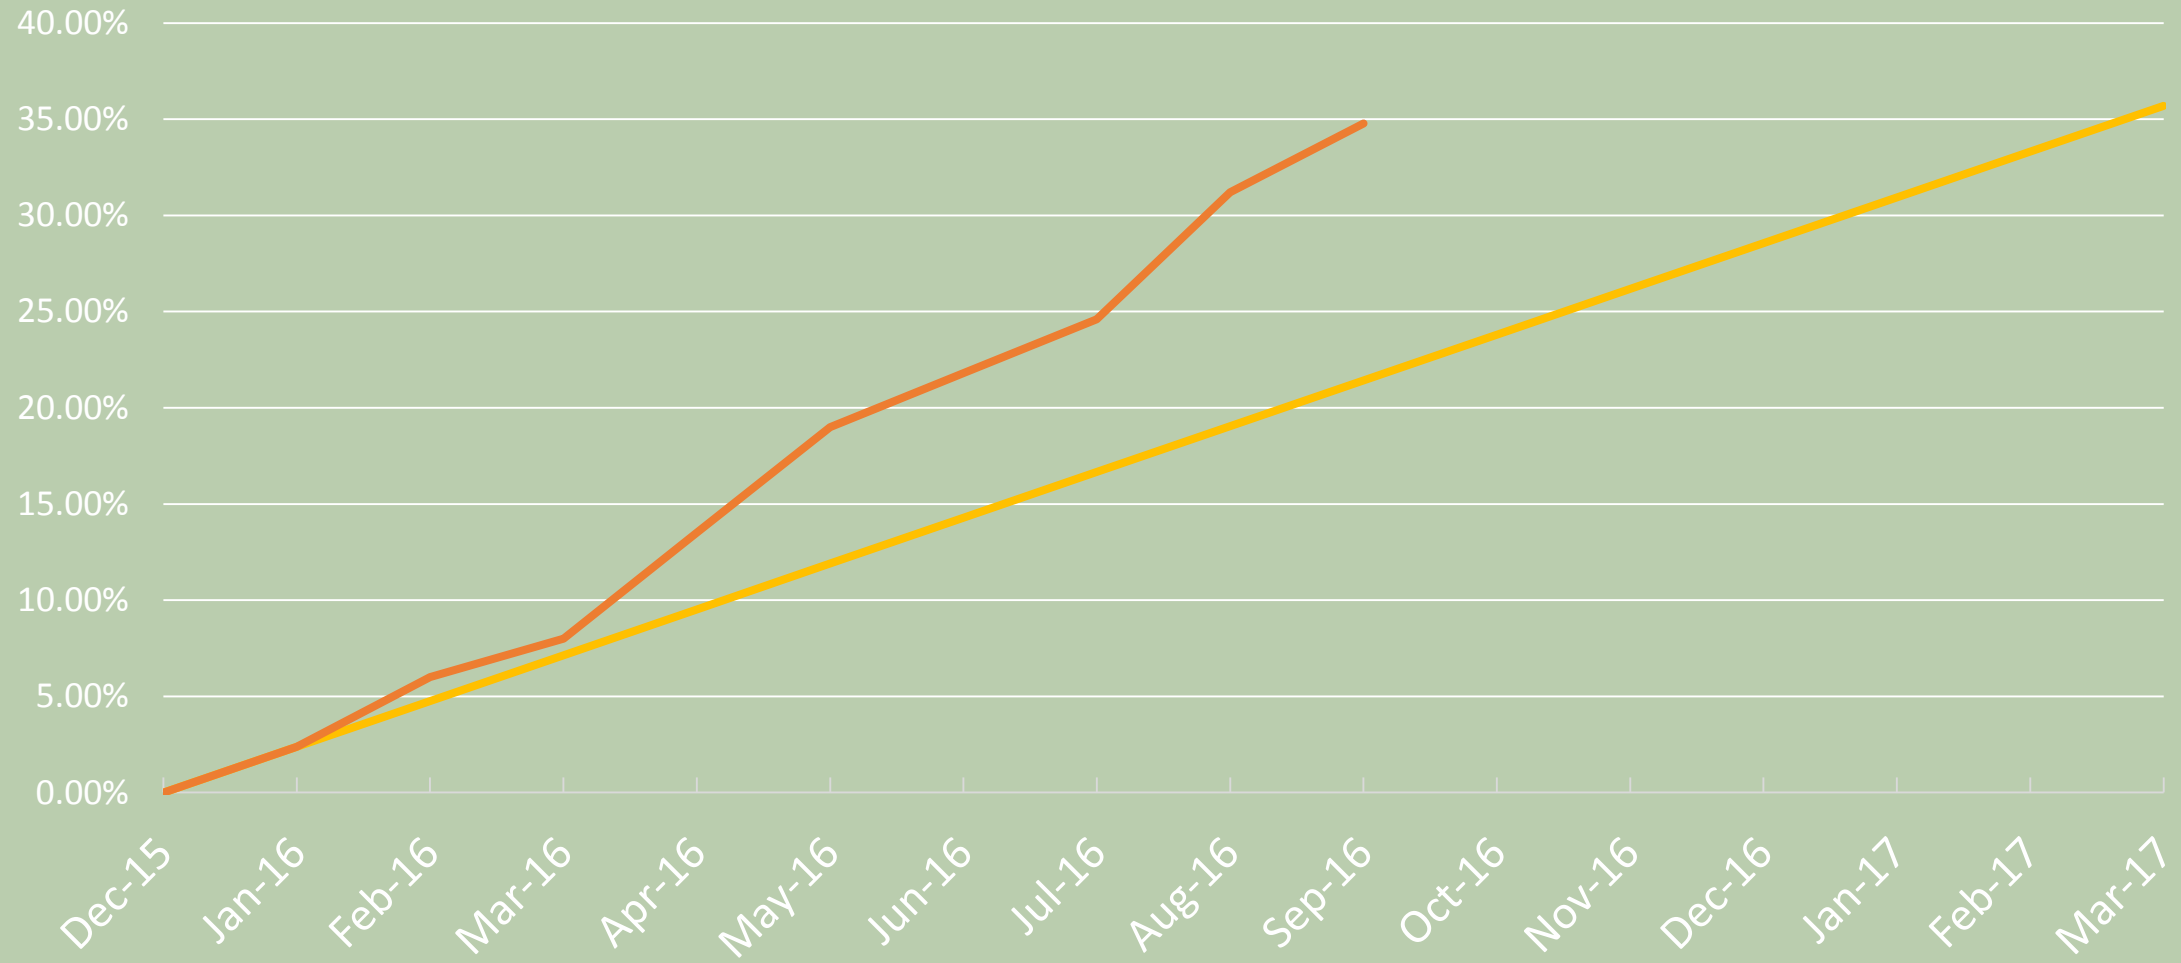

What to expect

- ✓ Paving on Martin Road bridge approaches (*complete*)
- ✓ Traffic switched to completed south portion of Martin Road bridge (*Aug. 15*)
- ❑ Removal of old Martin Road bridge (*Began Aug. 21, continuing each night Sundays through Thursdays with lane reductions on Memorial Parkway 9 p.m. to 5 a.m.*)
- ✓ Paving on northbound Memorial Parkway service road (*complete*)
- ✓ Paving on southbound Memorial Parkway service road (*near complete*)

What to expect, continued

- ❑ Traffic switched to service roads (*anticipated Aug. 31*)
 - Left turns from service roads to Logan Drive and Lily Flagg Road functioning
 - All median crossovers closed; U-turns can be made at Golf Road, Byrd Spring Road, Logan Drive/Lily Flagg Road and Whitesburg Drive
- ❑ Southbound ramp from Martin Road (*anticipated late September*)
- ❑ Begin construction of Phase II overpasses (*anticipated this year*)
 - No impact on Phase I traffic expected

Martin Road bridge

Now



In the future






*Photo taken
prior to
completion of
eastbound
(south) portion
of new Martin
Road bridge

Elevated,
signalized
service road
intersection


Mainline
travels under
Martin Road
bridge

Additional
movements
available for
traffic in
all directions


Additional
eastbound and
westbound
lanes

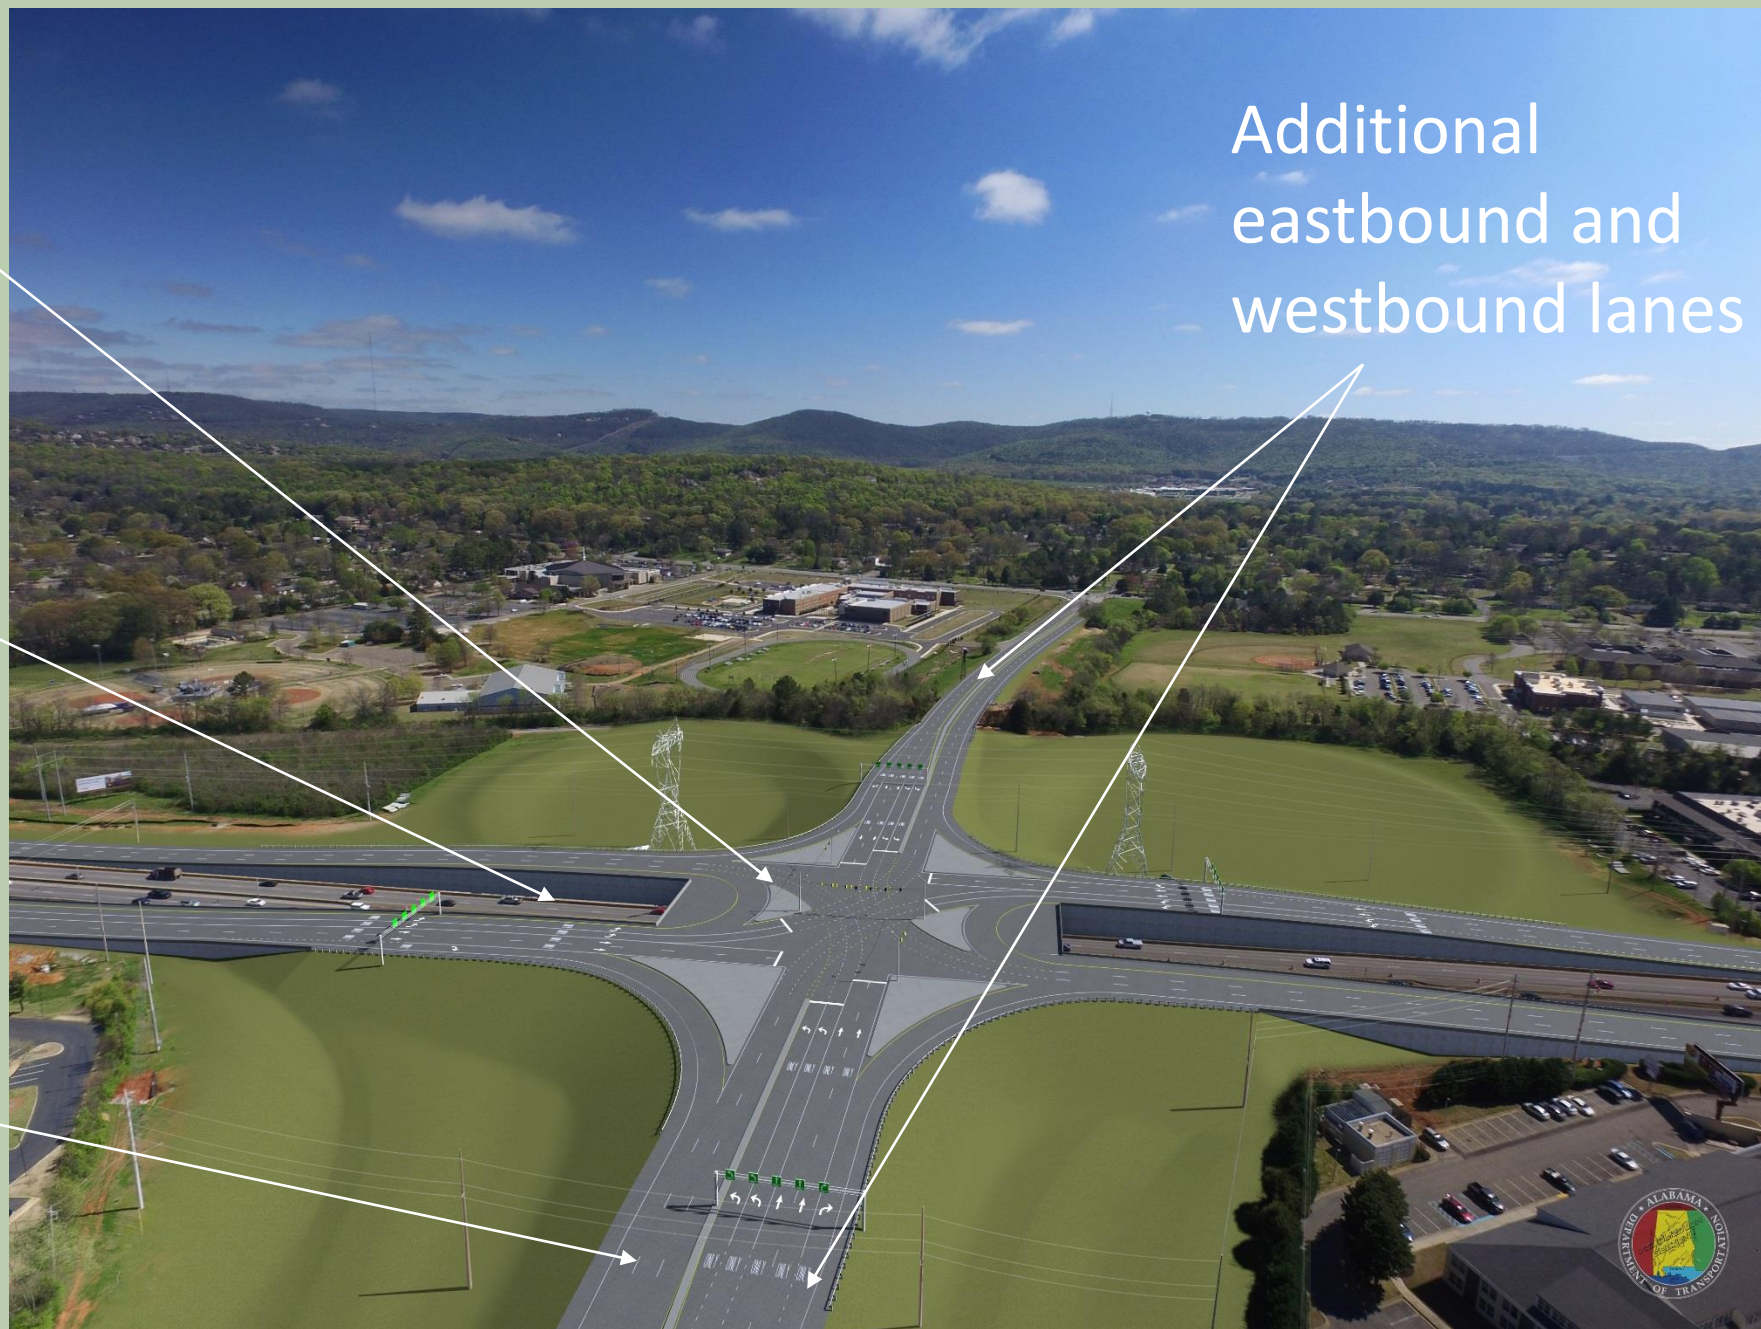

Benaroya Connector

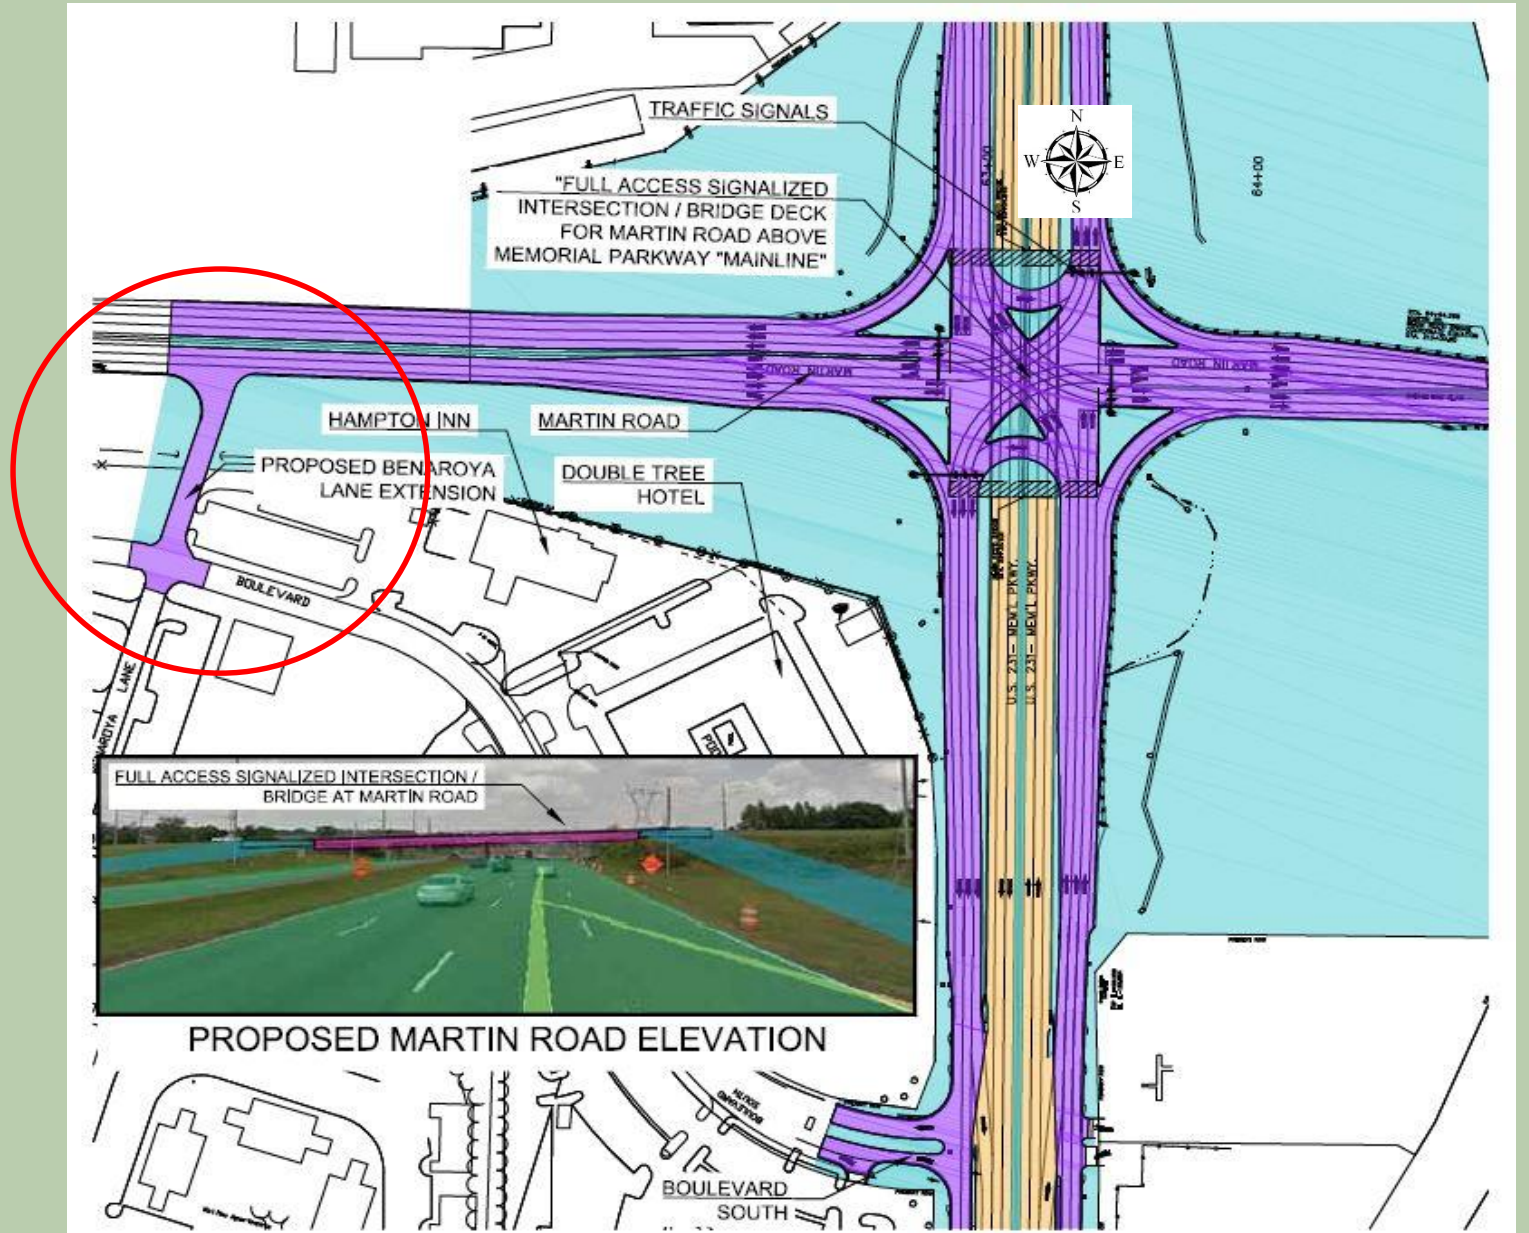

- Adding right in/right out connection from Martin Road to Boulevard South
- Construction started today and will be complete in mid-October

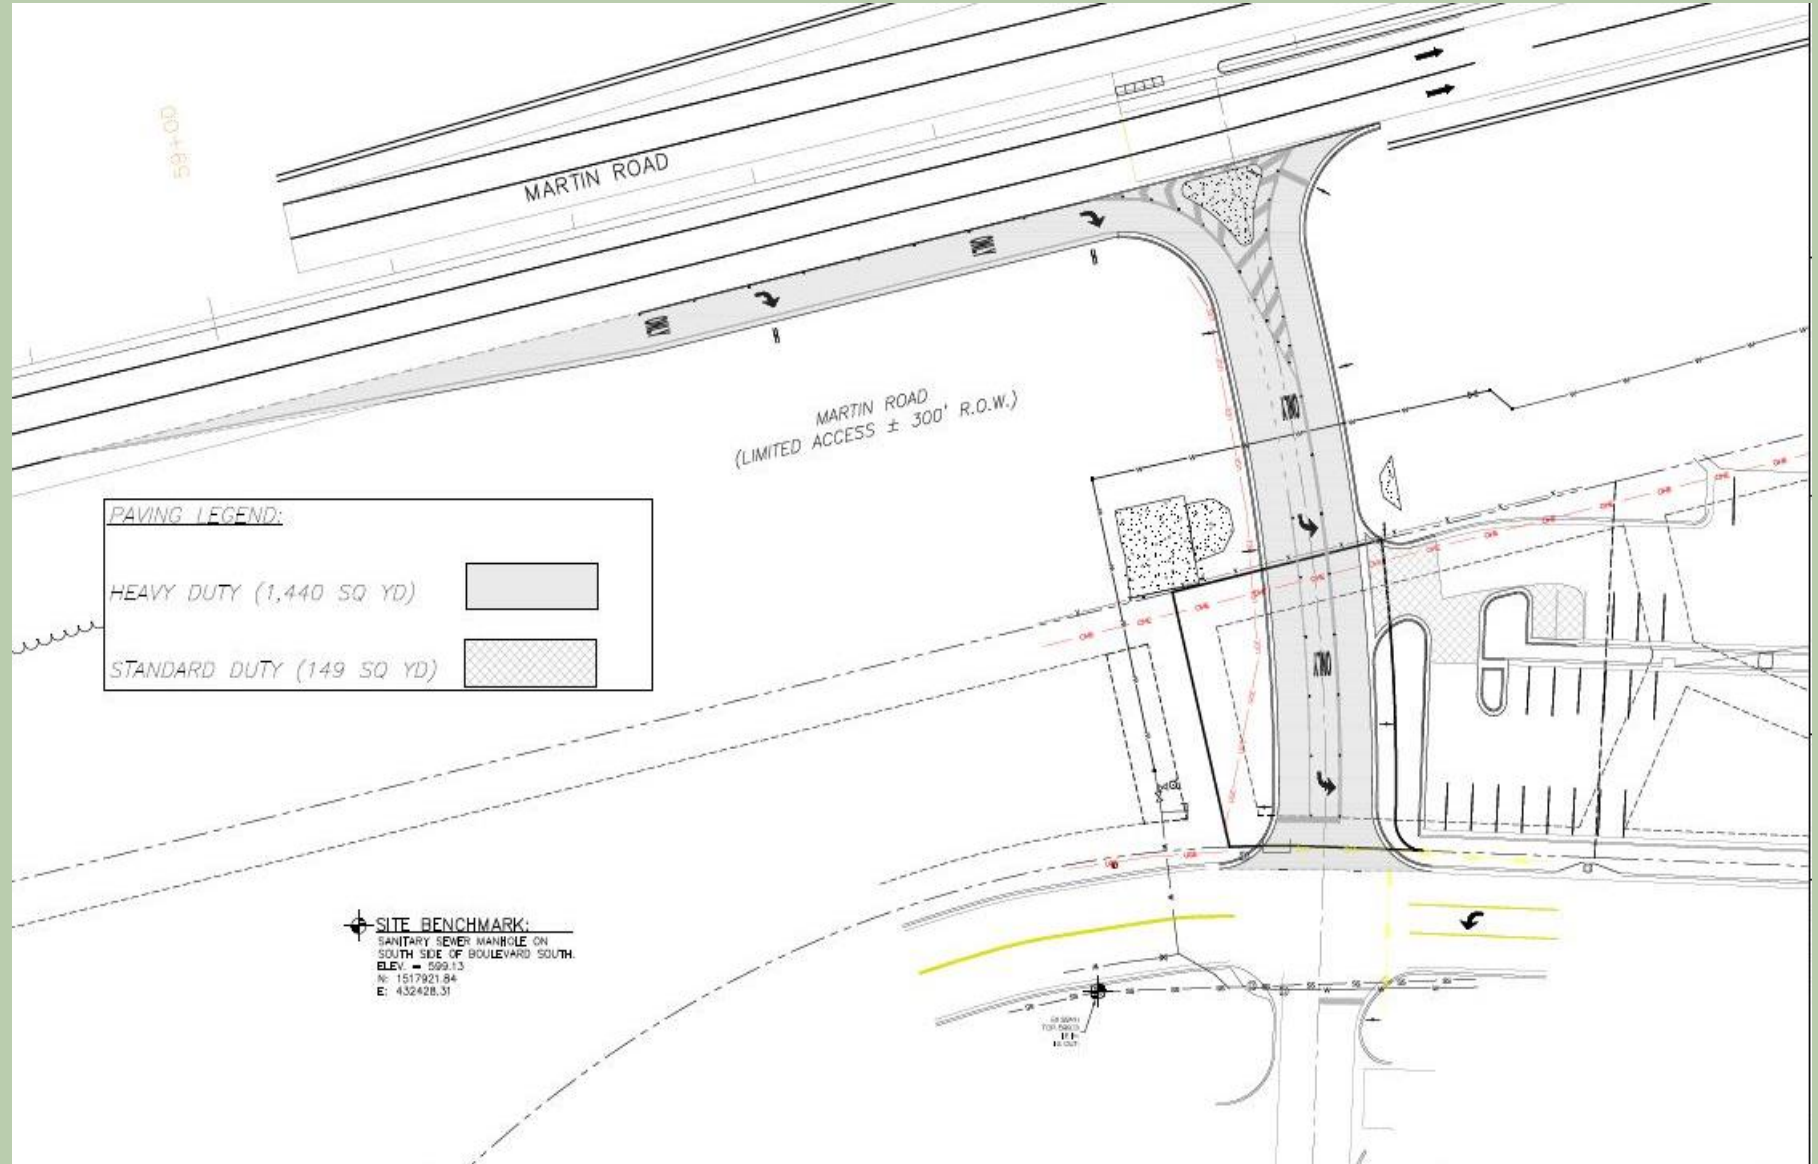

Contact

Seth Burkett

Public Information Specialist

256-505-4964

burketts@dot.state.al.us
